ANIMAL SHELTER DESIGN BUILD SCHEDULE

ID	Task Name	Duration	Start
1	Policy and Overview Board Business	0 days	Tue 4/12/16
2	RFP for Construction Management Firm	22 days	Tue 4/12/16
3	Construction Management Selection and Contract	50 days	Thu 5/12/16
4	CM development of D/B package and schedule	22 days	Thu 7/21/16
5	RFP for Master Architect	15 days	Mon 8/22/16
6	Master Architect Selection and Contract	50 days	Mon 9/12/16
7	**Project Development Period**	**270 days**	**Mon 11/21/16**
8	Preparation of Bridging Documents	180 days	Mon 11/21/16
9	Topo Mapping	25 days	Mon 11/21/16
10	Geotech Assessment	25 days	Mon 11/21/16
11	Plan Permit Issuance	10 days	Mon 7/31/17
12	Utility Coordination	90 days	Mon 7/31/17
13	Board Authorization for stipend/pre-qualification of D/B team	10 days	Mon 8/14/17
14	Pre-Qualification of D/B Teams	22 days	Mon 8/28/17
15	D/B Team selection process	60 days	Wed 9/27/17
16	D/B subcontractors	15 days	Wed 12/20/17
17	Notice to Proceed	0 days	Tue 1/9/18

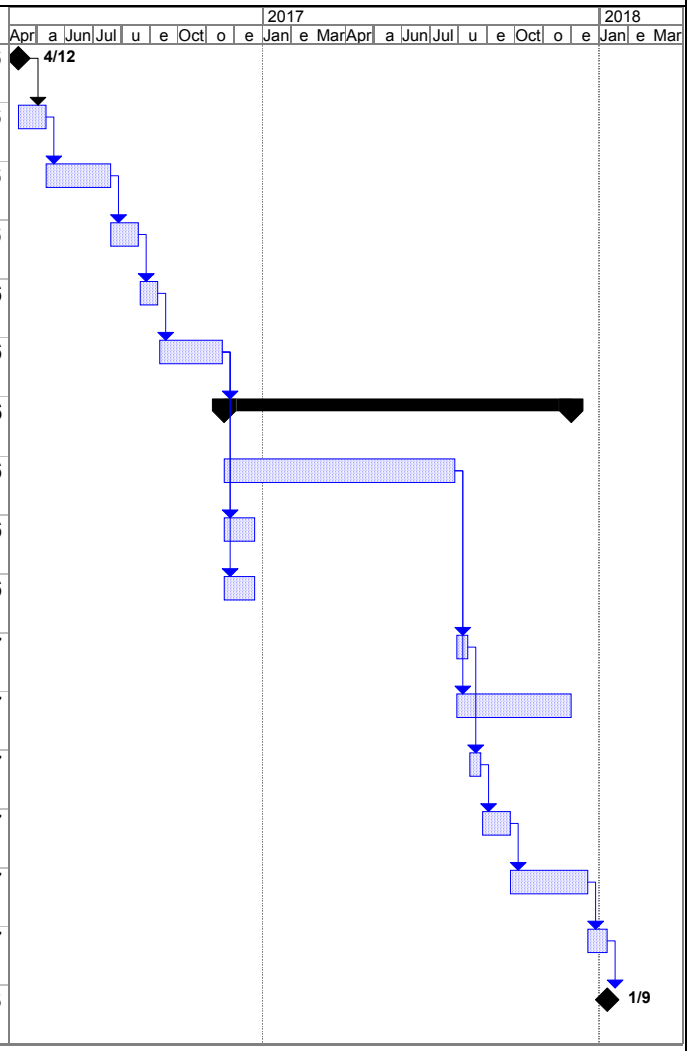

Project: design build schedule
Date: Mon 2/22/16

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
